

FBCM Building Work as of 4/2022

Contractor: Steven Czerwinski, Inc.
Work Description

Replace wood areas with vinyl siding and appropriate molding around windows
New Soffit material
Wrap all rakes and fascias in white aluminum as needed

Contracted/In Progress	Area to be Worked	Cost	Date Contracted	Deposit	Remaining \$ required to complete work	Work Completed
	Small Gabled Area	\$3,465.00	6/13/2021		\$67,445.67	X
	Large Gabled Area	\$7,654.68	6/13/2021		\$59,790.99	X
	Fellowship Hall Parking Lot Side	\$5,433.12	6/13/2021	\$1,067.00	\$54,357.87	X
	Back Entry Worship Center	\$2,102.76				
	Gable-Choir Rm walkway	\$2,441.34				
	Fellowship Hall Back Entry Area	\$2,786.85				
2023	Carpport Entry	\$3,150.18				
2023	Carpport overhang	out for \$				
	Hidden Entry Driveway Side	\$3,851.10				
	Front Entry Hillstown Road	\$2,811.60				
	Small Gabled Area to left of main entry	out for \$				
	Roof Peak over Welcome Area	out for \$				
	Choir Room Walk Way	\$3,158.10				
	Play Area (Soffit Only)	\$2,480.94				
2022	Remaining Roof Replacement	\$31,575.00			(looking at a few week lead time once booked)	
	Total of Proposed Bldg Work	\$70,910.67				


Note: Bldg Work will need to be requoted due to age of quotes due to pricing increases (approx. 20%+).


Money Approved at 6.21 Business Meeting	\$16,000.00
Total Work Contracted 6.18.21 *	\$16,552.80

*Will take overage from Building and Maintenance Budget

NOTES:

1. There are three additional areas out for pricing.
2. One outstanding section is the flat roof section over Welcome Enter and carpport. The material used for that area is unavailable at this time. Will quote when materials are available.

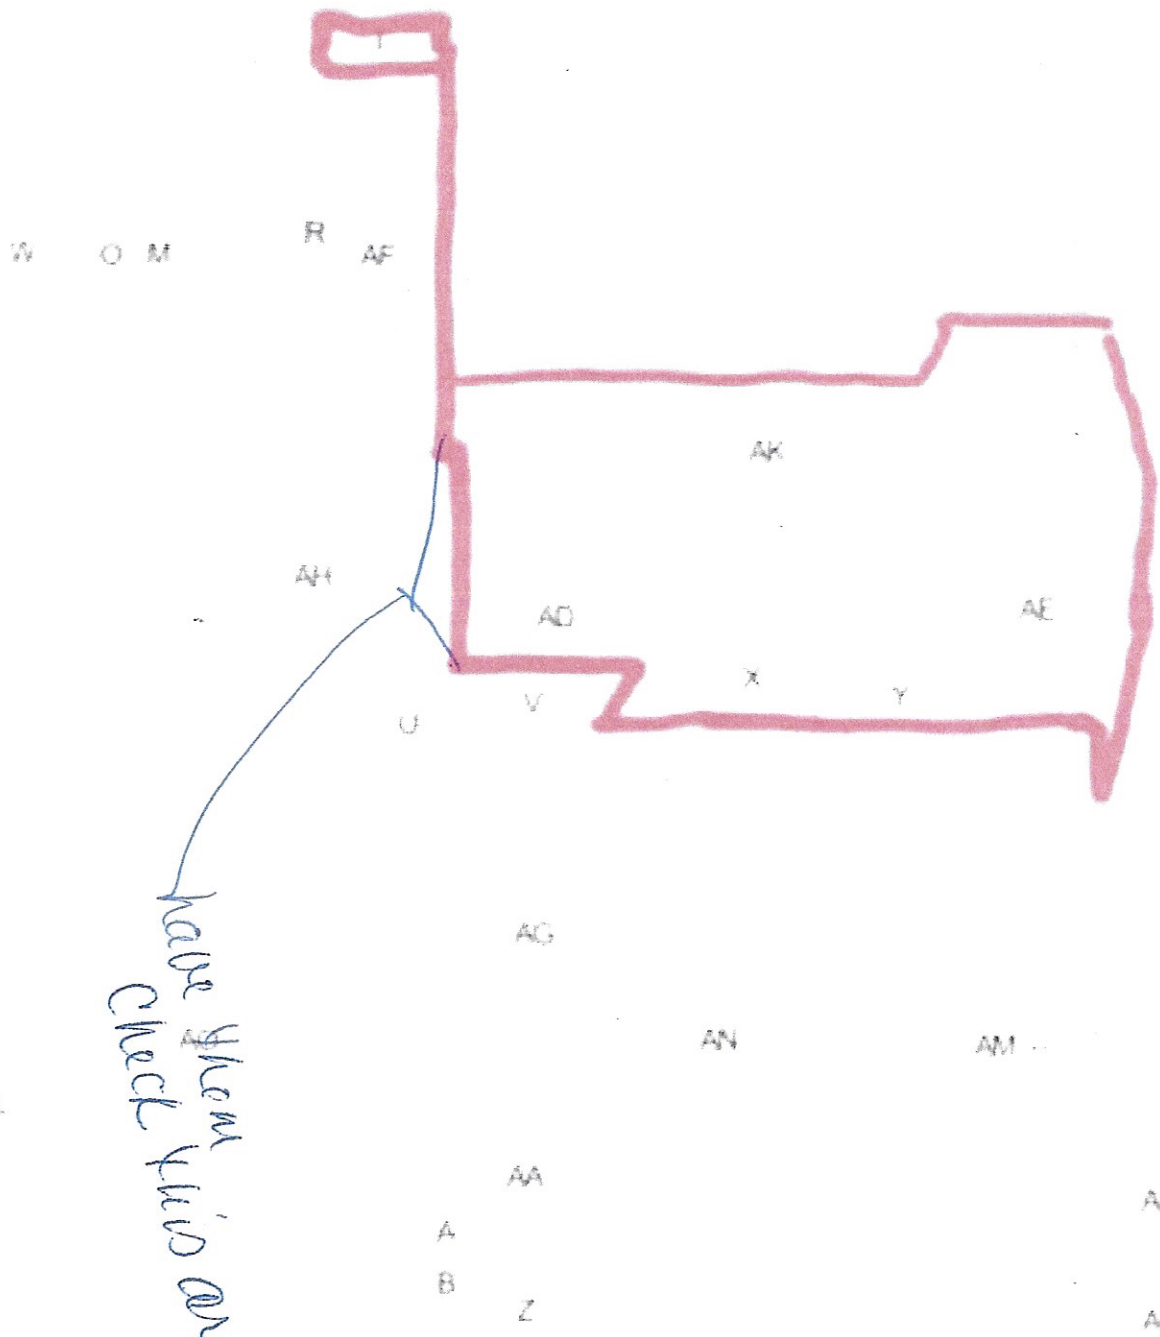

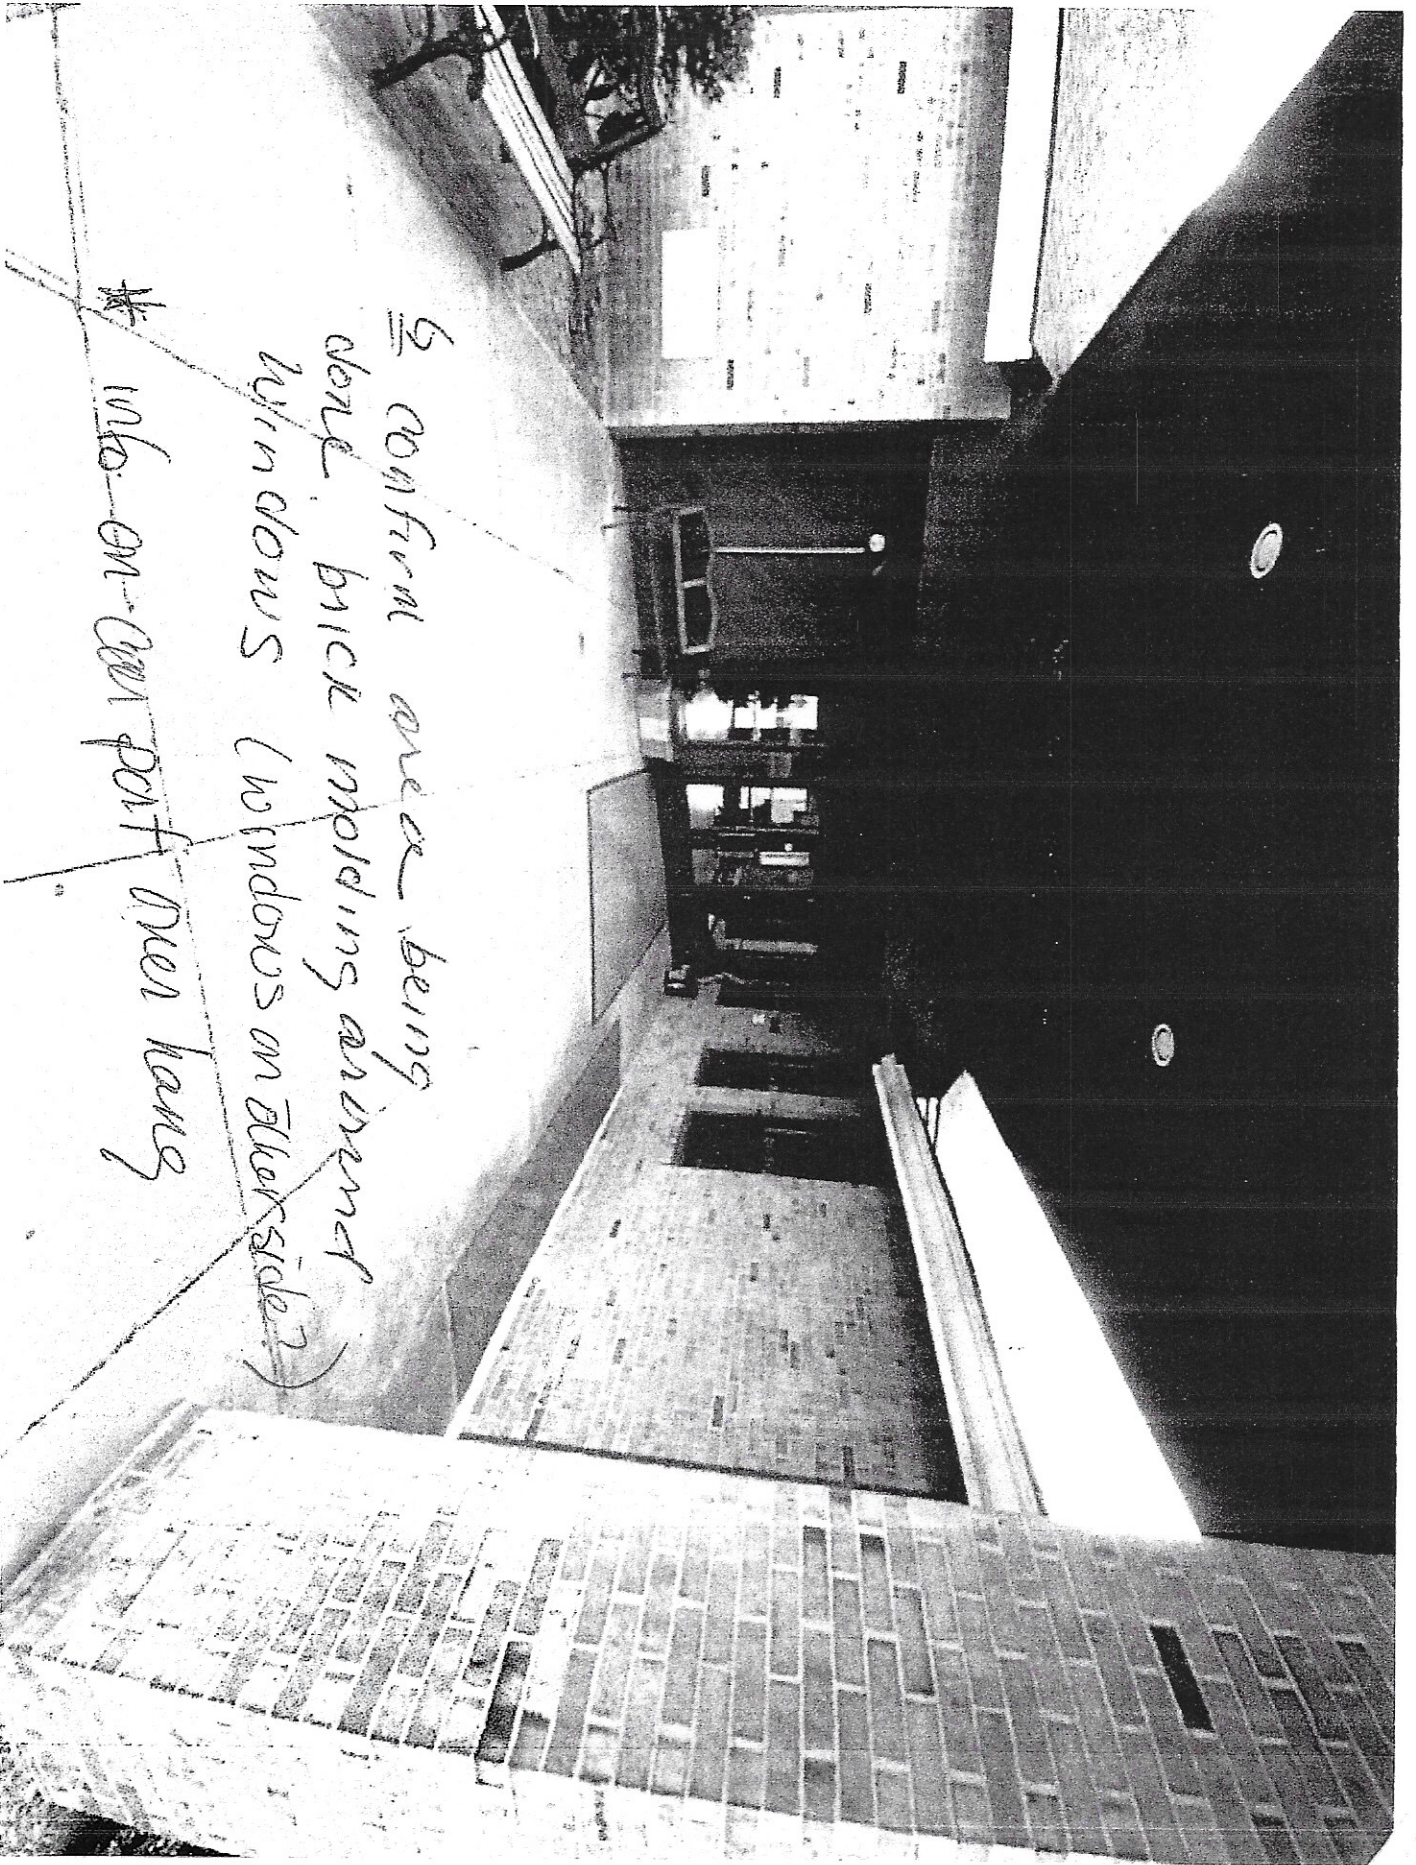

to confirm order being
done. brick molding around
windows (windows on other side?)
* info on cur part over hang
